

### ACTIVITY SCHEDULE

|                           | MONTHS FROM START OF CONSTRUCTION |   |   |   |   |   |
|---------------------------|-----------------------------------|---|---|---|---|---|
|                           | 1                                 | 2 | 3 | 4 | 5 | 6 |
| CLEARING FOR BMPs         | █                                 |   |   |   |   |   |
| SEDIMENT CONTROL          | █                                 | █ | █ | █ | █ | █ |
| MAINTAIN EROSION CONTROL  | █                                 | █ | █ | █ | █ | █ |
| EARTHWORK                 |                                   | █ | █ | █ | █ | █ |
| BUILDING CONSTRUCTION     |                                   |   | █ | █ | █ | █ |
| TEMPORARY GRASSING        |                                   |   | █ | █ | █ | █ |
| FINAL GRASS LANDSCAPE     |                                   |   |   |   | █ | █ |
| PAVING                    |                                   |   |   |   |   | █ |
| REMOVAL OF TEMPORARY BMPs |                                   |   |   |   |   | █ |

CONSTRUCTION SCHEDULED TO BEGIN ON 4/7/25  
AND BE COMPLETED ON OR BEFORE 10/7/25

### CONSTRUCTION SEQUENCE (FINAL PHASE)

1. MAINTAIN ALL INSTALLED BMP'S. REMOVE SEDIMENT AS REQUIRED. MAINTAIN MONITORING PROGRAM.
2. COMPLETE GRADING OPERATIONS AND STABILIZE ALL DISTURBED AREAS WITH THE APPROPRIATE PERMANENT VEGETATION OR OTHER SURFACE TREATMENT. INSTALL MATTING ON ALL POND SLOPES AND 4" OF STRAW ON ALL OTHER DISTURBED AREAS.
3. REMOVE CONCRETE WASHOUT BASIN. STABILIZE THE AREA WITH THE APPROPRIATE PERMANENT VEGETATION.
4. ONCE FINAL STABILIZATION HAS BEEN ACHIEVED IN ALL OTHER AREAS, REMOVE PERIMETER SILT FENCE AND CONSTRUCTION EXITS. STABILIZE THESE AREAS WITH THE APPROPRIATE PERMANENT VEGETATION. BY DEFINITION, FINAL STABILIZATION MEANS THAT ALL SOIL DISTURBING ACTIVITIES AT THE SITE HAVE BEEN COMPLETED, AND THAT FOR UNPAVED AREAS AND AREAS NOT COVERED BY PERMANENT STRUCTURES AND AREAS LOCATED OUTSIDE THE WASTE DISPOSAL LIMITS OF A LANDFILL CELL THAT HAS BEEN CERTIFIED BY EPD FOR WASTE DISPOSAL, 100% OF THE SOIL SURFACE IS UNIFORMLY COVERED IN PERMANENT VEGETATION WITH A DENSITY OF 70% OR GREATER, OR LANDSCAPED ACCORDING TO THE PLAN (UNIFORMLY COVERED WITH LANDSCAPING MATERIALS IN PLANNED LANDSCAPED AREAS), OR EQUIVALENT PERMANENT STABILIZATION MEASURES AS DEFINED IN THE MANUAL (EXCLUDING A CROP OF ANNUAL VEGETATION AND SEEDING OF TARGET CROP PERENNIALS APPROPRIATE FOR THE REGION).




NOTE: AT THE END OF EACH DAY, CONSTRUCT A SAFETY FENCE AROUND ALL SEDIMENT BASINS OR TRAPS, DITCHES, TRENCHES, HOLES, ETC. WITH 2:1 OR STEEPER SLOPES AND A DEPTH GREATER THAN 24".

### HYDROLOGY SUMMARY


EXISTING:  
 $Q_{25}=70.44$  cfs  
 $Q_{25}=167.24$  cfs

PROPOSED:  
 $Q_{25}=28.48$  cfs  
 $Q_{25}=60.22$  cfs

SEE HYDROLOGY STUDY PREPARED BY RICHARDS & ASSOCIATES, DATED 3/24/25.

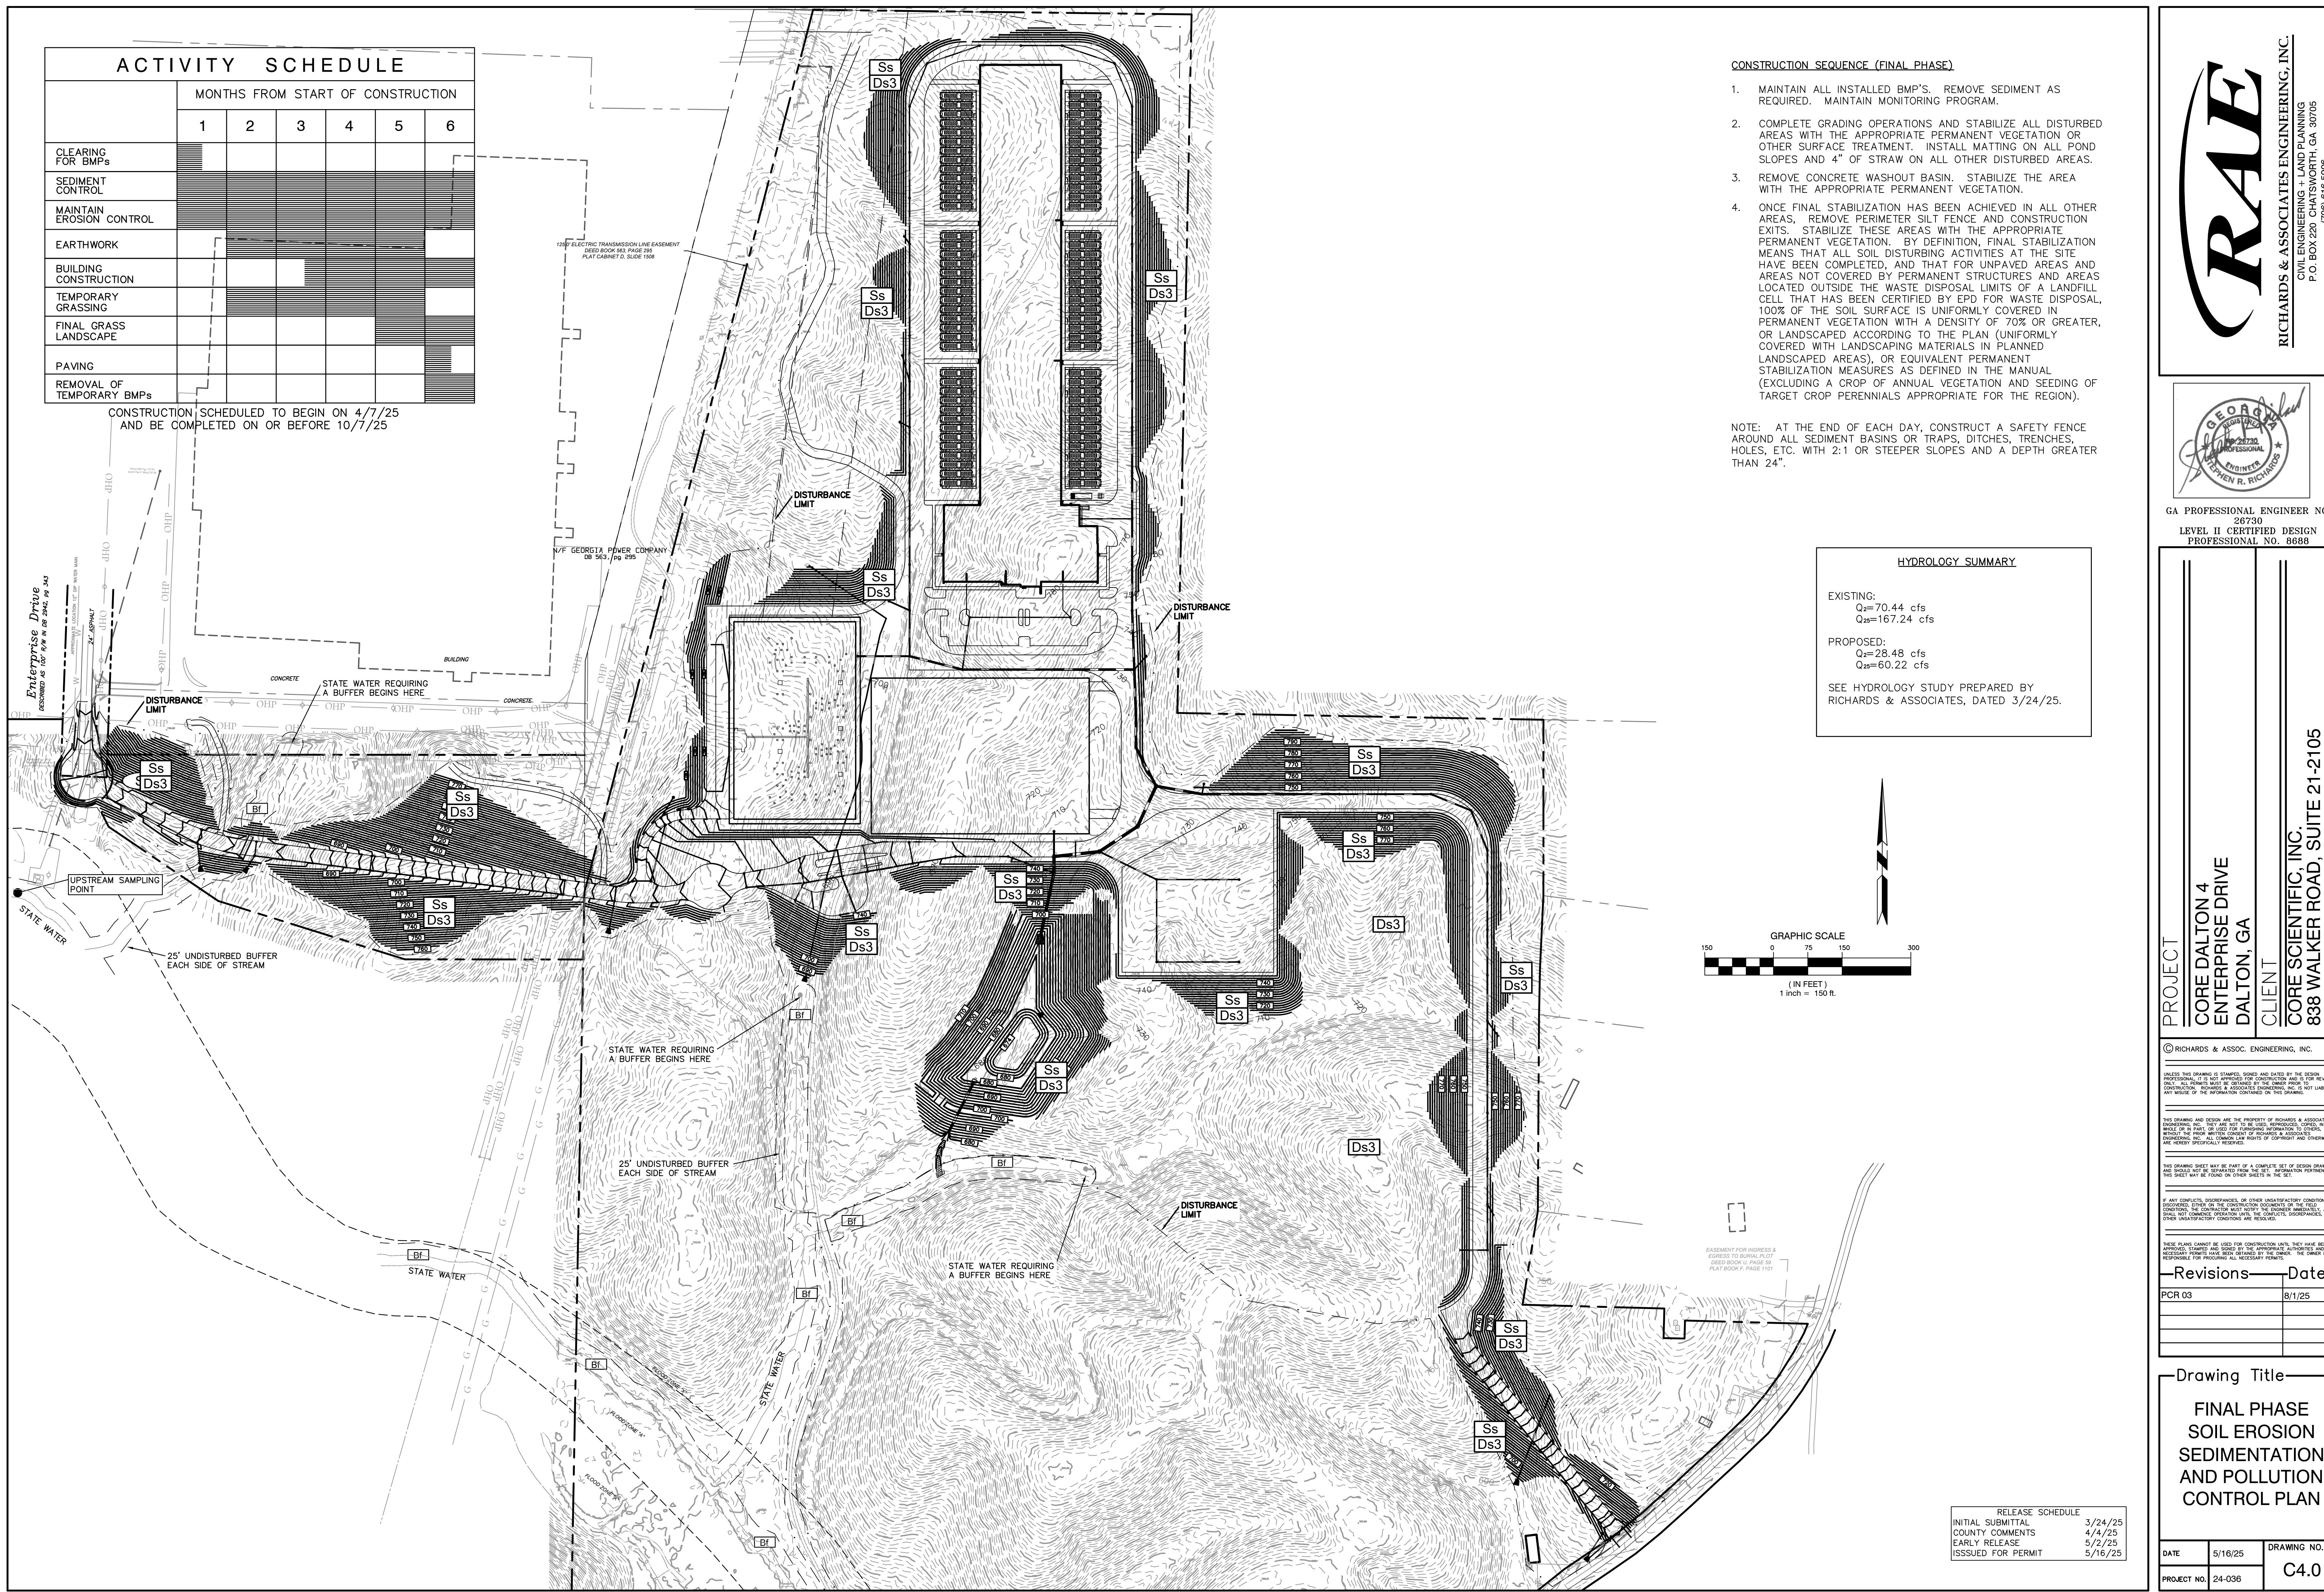

**RAE**  
 RICHARDS & ASSOCIATES ENGINEERING, INC.  
 CIVIL ENGINEERING + LAND PLANNING  
 P.O. BOX 220 CHATSWORTH, GA 30705  
 (706) 616-9506



GA PROFESSIONAL ENGINEER NO. 26730  
 LEVEL II CERTIFIED DESIGN PROFESSIONAL NO. 8688

PROJECT  
**CORE DALTON 4**  
**ENTERPRISE DRIVE**  
**DALTON, GA**  
 CLIENT  
**CORE SCIENTIFIC, INC.**  
**838 WALKER ROAD, SUITE 21-2105**  
**DOVER, DE 19904**

© RICHARDS & ASSOC. ENGINEERING, INC.

UNLESS THIS DRAWING IS STAMPED, SIGNED AND DATED BY THE DESIGN PROFESSIONAL, IT IS NOT VALID. THE DESIGN PROFESSIONAL IS NOT RESPONSIBLE FOR THE CONSTRUCTION OF THIS PROJECT. RICHARDS & ASSOCIATES ENGINEERING, INC. IS NOT LIABLE FOR ANY MISTAKE OR OMISSION OF INFORMATION CONTAINED ON THIS DRAWING.

THIS DRAWING AND DESIGN ARE THE PROPERTY OF RICHARDS & ASSOCIATES ENGINEERING, INC. AND SHALL BE KEPT IN CONFIDENCE. NO PART OF THIS DRAWING OR DESIGN SHALL BE REPRODUCED OR TRANSMITTED IN ANY FORM OR BY ANY MEANS, ELECTRONIC OR MECHANICAL, INCLUDING PHOTOCOPYING, RECORDING, OR BY ANY INFORMATION STORAGE AND RETRIEVAL SYSTEM, WITHOUT THE WRITTEN CONSENT OF RICHARDS & ASSOCIATES ENGINEERING, INC. ALL RIGHTS OF COPYRIGHT AND OTHERWISE ARE HEREBY SPECIFICALLY RESERVED.

THIS DRAWING SHEET MAY BE PART OF A COMPLETE SET OF DESIGN DRAWINGS AND SHOULD NOT BE SEPARATED FROM THE SET. INFORMATION PERTAINING TO THIS SHEET MAY BE FOUND ON OTHER SHEETS IN THE SET.

IF ANY CONFLICTS, DISCREPANCIES, OR OTHER UNSATISFACTORY CONDITIONS ARE DISCOVERED EITHER ON THE CONSTRUCTION DOCUMENTS OR IN THE FIELD, THE CONTRACTOR MUST NOTIFY THE ENGINEER IMMEDIATELY AND SHALL NOT COMMENCE OPERATIONS UNTIL THE CONTRACTOR, DISCREPANCIES, OR OTHER UNSATISFACTORY CONDITIONS ARE RESOLVED.

THESE PLANS CANNOT BE USED FOR CONSTRUCTION UNLESS THEY HAVE BEEN APPROVED, SIGNED AND SEALED BY THE APPROPRIATE AUTHORITIES AND ALL NECESSARY PERMITS HAVE BEEN OBTAINED BY THE OWNER. THE OWNER IS RESPONSIBLE FOR PROVIDING ALL NECESSARY PERMITS.

| Revisions | Date   |
|-----------|--------|
| PCR 03    | 8/1/25 |
|           |        |
|           |        |

Drawing Title  
**FINAL PHASE**  
**SOIL EROSION**  
**SEDIMENTATION**  
**AND POLLUTION**  
**CONTROL PLAN**

| DATE        | 5/16/25 | DRAWING NO. |
|-------------|---------|-------------|
| PROJECT NO. | 24-036  | C4.0        |

| RELEASE SCHEDULE  |         |
|-------------------|---------|
| INITIAL SUBMITTAL | 3/24/25 |
| COUNTY COMMENTS   | 4/4/25  |
| EARLY RELEASE     | 5/2/25  |
| ISSUED FOR PERMIT | 5/16/25 |
